

ID	Task Name	Duration	Start	Finish
1	Migrate SECNAV in the Pentagon to DNHN	118d	Wed 12/11/96	Thu 5/22/97
2	Collect Requirements	25d	Wed 12/11/96	Tue 1/14/97
3	Collect SECNAV LAN Requirements	25d	Wed 12/11/96	Tue 1/14/97
4	Perform Migration Kick-off Meeting	1d	Wed 12/11/96	Wed 12/11/96
5	Schedule Site Surveys	12d	Mon 12/16/96	Tue 12/31/96
6	Perform Site Surveys	12d	Mon 12/16/96	Tue 12/31/96
7	Create Technical Reports	12d	Mon 12/16/96	Tue 12/31/96
8	Submit Technical Reports for Review	1d	Fri 1/10/97	Fri 1/10/97
9	Receive Accepted Technical Reports	1d	Mon 1/13/97	Mon 1/13/97
10	Finalize Technical Reports	1d	Tue 1/14/97	Tue 1/14/97
11	Consolidate Requirements	11d	Wed 1/15/97	Wed 1/29/97
12	Consolidate SECNAV Requirements	1d	Wed 1/15/97	Wed 1/15/97
13	Group Reports by Server	1d	Wed 1/15/97	Wed 1/15/97
14	List Applications	1d	Wed 1/15/97	Wed 1/15/97
15	List Hardware on Each Server	1d	Wed 1/15/97	Wed 1/15/97
16	List Users	1d	Wed 1/15/97	Wed 1/15/97
17	List Data and Print Shares	1d	Wed 1/15/97	Wed 1/15/97
18	Collect Workstation Data	1d	Wed 1/15/97	Wed 1/15/97
19	List Number of Workstations	1d	Wed 1/15/97	Wed 1/15/97
20	List Types of Workstations	1d	Wed 1/15/97	Wed 1/15/97
21	Engineer New SECNAV Requirements	1d	Wed 1/29/97	Wed 1/29/97
22	List New Requirements by Server	1d	Wed 1/29/97	Wed 1/29/97
23	Assign Task to Groups	1d	Wed 1/29/97	Wed 1/29/97
24	Assign Due Dates	1d	Wed 1/29/97	Wed 1/29/97
25	Develop Migration Order	1d	Thu 2/6/97	Thu 2/6/97
26	Gather Server/Group Information	1d	Thu 2/6/97	Thu 2/6/97
27	Conduct Migration Schedule Mtg.	1d	Thu 2/6/97	Thu 2/6/97
28	Develop a Server Migration Order	1d	Thu 2/6/97	Thu 2/6/97
29	Engineer New Requirements	26d	Fri 2/7/97	Thu 3/13/97
30	Develop Solutions	26d	Fri 2/7/97	Thu 3/13/97
31	Fax out	26d	Fri 2/7/97	Thu 3/13/97

Project: SECNAV Migration without
Date: Thu 3/27/97

Task

Progress

Milestone

Summary

Rolled Up Task

Rolled Up Milestone

Rolled Up Progress

ID	Task Name	Duration	Start	Finish
32	Fax Server Training	1d	Fri 2/7/97	Fri 2/7/97
33	Dial Out	26d	Fri 2/7/97	Thu 3/13/97
34	Dial-out Training	1d	Fri 2/7/97	Fri 2/7/97
35	Naval Messages	26d	Fri 2/7/97	Thu 3/13/97
36	SECNAV Imaging	26d	Fri 2/7/97	Thu 3/13/97
37	REACT Printing	26d	Fri 2/7/97	Thu 3/13/97
38	LCTS	26d	Fri 2/7/97	Thu 3/13/97
39	cc:Mail Archives	26d	Fri 2/7/97	Thu 3/13/97
40	MTF Editor	26d	Fri 2/7/97	Thu 3/13/97
41	Document Translator	26d	Fri 2/7/97	Thu 3/13/97
42	WP Macros	26d	Fri 2/7/97	Thu 3/13/97
43	Schedule Printing	26d	Fri 2/7/97	Thu 3/13/97
44	ATOS	26d	Fri 2/7/97	Thu 3/13/97
45	Install WordPerfect 6.0 on DNHN Servers	1d	Fri 2/7/97	Fri 2/7/97
46	Develop SECNAV Migration Schedule	4d	Mon 3/17/97	Thu 3/20/97
47	Inform SECNAV Orgs of Migration Order	1d	Mon 3/17/97	Mon 3/17/97
48	Inform SECNAV Orgs of Solution	1d	Mon 3/17/97	Mon 3/17/97
49	Modify Solutions	3d	Mon 3/17/97	Wed 3/19/97
50	Develop Org Migration Schedule	1d	Thu 3/20/97	Thu 3/20/97
51	Publish Migration Schedule	1d	Thu 3/20/97	Thu 3/20/97
52	Train SECNAV	45d	Fri 3/21/97	Thu 5/22/97
53	Develop Training Plan	45d	Fri 3/21/97	Thu 5/22/97
54	Identify Training Requirements	1d	Fri 3/21/97	Fri 3/21/97
55	Coordinate Training Schedule to Migration Schedule	1d	Fri 3/21/97	Fri 3/21/97
56	Inform SECNAV of Training	1d	Fri 3/21/97	Fri 3/21/97
57	Schedule Training	40d	Fri 3/21/97	Thu 5/15/97
58	Train SECNAV Organizations	45d	Fri 3/21/97	Thu 5/22/97
59	Upgrade Infrastructure	9d	Wed 2/19/97	Mon 3/3/97
60	Install DNHN Firewall	9d	Wed 2/19/97	Mon 3/3/97
61	Install New Servers	4d	Wed 2/26/97	Mon 3/3/97
62	Migrate SECNAV Orgs	33d	Tue 3/4/97	Wed 4/16/97

Project: SECNAV Migration without
Date: Thu 3/27/97

Task

Progress

Milestone

Summary

Rolled Up Task

Rolled Up Milestone

Rolled Up Progress

ID	Task Name	Duration	Start	Finish
63	Migrate FS11, CHINFO	4d	Tue 3/4/97	Fri 3/7/97
64	Build Server Resources	1d	Tue 3/4/97	Tue 3/4/97
65	Build CHINFO User Accounts/User Groups	1d	Tue 3/4/97	Tue 3/4/97
66	Build CHINFO Printer Queues	1d	Tue 3/4/97	Tue 3/4/97
67	Build Required Exchange Public Folders	1d	Tue 3/4/97	Tue 3/4/97
68	Build Required NT Shares	1d	Tue 3/4/97	Tue 3/4/97
69	Migrate cc:Mail	1d	Fri 3/7/97	Fri 3/7/97
70	Update Exchange Accounts w/ cc:Mail Inf.	1d	Fri 3/7/97	Fri 3/7/97
71	Migrate cc:Mail server Inf.	1d	Fri 3/7/97	Fri 3/7/97
72	Forward cc:Mail to Exchange Accounts	1d	Fri 3/7/97	Fri 3/7/97
73	Migrate SECNAV Server Data	1d	Fri 3/7/97	Fri 3/7/97
74	Migrate CHINFO Group Data Shares	1d	Fri 3/7/97	Fri 3/7/97
75	Migrate CHINFO Data Shares	1d	Fri 3/7/97	Fri 3/7/97
76	Modify CHINFO User Workstations	3d	Fri 3/7/97	Mon 3/10/97
77	Configure Workstations	2d	Fri 3/7/97	Sat 3/8/97
78	Remove SECNAV PC Image	2d	Fri 3/7/97	Sat 3/8/97
79	Install DNHN PC Image	2d	Fri 3/7/97	Sat 3/8/97
80	Install Exchange SP2	2d	Fri 3/7/97	Sat 3/8/97
81	Q/A CHINFO PCs	1d	Mon 3/10/97	Mon 3/10/97
82	Log Into DNHN	1d	Mon 3/10/97	Mon 3/10/97
83	Log into Exchange	1d	Mon 3/10/97	Mon 3/10/97
84	Map and Print to CHINFO DNHN Printers	1d	Mon 3/10/97	Mon 3/10/97
85	Test Applications	1d	Mon 3/10/97	Mon 3/10/97
86	Sign off On PCs	1d	Mon 3/10/97	Mon 3/10/97
87	Migrate FS5, M&RA	5d	Wed 3/19/97	Tue 3/25/97
88	Build Server Resources	4d	Wed 3/19/97	Mon 3/24/97
89	Build M&RA User Accounts/User Groups	4d	Wed 3/19/97	Mon 3/24/97
90	Build M&RA Printer Queues	4d	Wed 3/19/97	Mon 3/24/97
91	Build Required Exchange Public Folders	4d	Wed 3/19/97	Mon 3/24/97
92	Build Required NT Shares	4d	Wed 3/19/97	Mon 3/24/97
93	Migrate cc:Mail	1d	Tue 3/25/97	Tue 3/25/97

Project: SECNAV Migration without
Date: Thu 3/27/97

Task

Progress

Milestone

Summary

Rolled Up Task

Rolled Up Milestone

Rolled Up Progress

ID	Task Name	Duration	Start	Finish
94	Update Exchange Accounts w/ cc:Mail Inf.	1d	Tue 3/25/97	Tue 3/25/97
95	Migrate cc:Mail server Inf.	1d	Tue 3/25/97	Tue 3/25/97
96	Forward cc:Mail to Exchange Accounts	1d	Tue 3/25/97	Tue 3/25/97
97	Migrate SECNAV Server Data	1d	Tue 3/25/97	Tue 3/25/97
98	Migrate M&RA Group Data Shares	1d	Tue 3/25/97	Tue 3/25/97
99	Migrate M&RA Data Shares	1d	Tue 3/25/97	Tue 3/25/97
100	Modify M&RA User Workstations	2d	Tue 3/25/97	Wed 3/26/97
101	Configure Workstations	1d	Tue 3/25/97	Tue 3/25/97
102	Remove SECNAV PC Image	1d	Tue 3/25/97	Tue 3/25/97
103	Install DNHN PC Image	1d	Tue 3/25/97	Tue 3/25/97
104	Install Exchange SP2	1d	Tue 3/25/97	Tue 3/25/97
105	Q/A M&RA PCs	1d	Wed 3/26/97	Wed 3/26/97
106	Log Into DNHN	1d	Wed 3/26/97	Wed 3/26/97
107	Log into Exchange	1d	Wed 3/26/97	Wed 3/26/97
108	Map and Print to M&RA DNHN Printers	1d	Wed 3/26/97	Wed 3/26/97
109	Test Applications	1d	Wed 3/26/97	Wed 3/26/97
110	Sign off On PCs	1d	Wed 3/26/97	Wed 3/26/97
111	Migrate FS1	4d	Mon 3/24/97	Thu 3/27/97
112	Build Server Resources	3d	Mon 3/24/97	Wed 3/26/97
113	Build FS1 User Accounts/User Groups	3d	Mon 3/24/97	Wed 3/26/97
114	Build FS1Printer Queues	3d	Mon 3/24/97	Wed 3/26/97
115	Build Required Exchange Public Folders	3d	Mon 3/24/97	Wed 3/26/97
116	Build Required NT Shares	3d	Mon 3/24/97	Wed 3/26/97
117	Migrate cc:Mail	1d	Thu 3/27/97	Thu 3/27/97
118	Update Exchange Accounts w/ cc:Mail Inf.	1d	Thu 3/27/97	Thu 3/27/97
119	Migrate cc:Mail server Inf.	1d	Thu 3/27/97	Thu 3/27/97
120	Forward cc:Mail to Exchange Accounts	1d	Thu 3/27/97	Thu 3/27/97
121	Migrate SECNAV Server Data	1d	Thu 3/27/97	Thu 3/27/97
122	Migrate FS1 Group Data Shares	1d	Thu 3/27/97	Thu 3/27/97
123	Migrate FS1 Data Shares	1d	Thu 3/27/97	Thu 3/27/97
124	Modify FS1 User Workstations	2d	Thu 3/27/97	Fri 3/28/97

Project: SECNAV Migration without
Date: Thu 3/27/97

Task

Progress

Milestone








Summary

Rolled Up Task

Rolled Up Milestone

Rolled Up Progress

ID	Task Name	Duration	Start	Finish
125	Configure Workstations	1d	Thu 3/27/97	Thu 3/27/97
126	Remove SECNAV PC Image	1d	Thu 3/27/97	Thu 3/27/97
127	Install DNHN PC Image	1d	Thu 3/27/97	Thu 3/27/97
128	Install Exchange SP2	1d	Thu 3/27/97	Thu 3/27/97
129	Q/A FS1 PCs	1d	Fri 3/28/97	Fri 3/28/97
130	Log Into DNHN	1d	Fri 3/28/97	Fri 3/28/97
131	Log into Exchange	1d	Fri 3/28/97	Fri 3/28/97
132	Map and Print to FS1DNHN Printers	1d	Fri 3/28/97	Fri 3/28/97
133	Test Applications	1d	Fri 3/28/97	Fri 3/28/97
134	Sign off On PCs	1d	Fri 3/28/97	Fri 3/28/97
135	Migrate FS2,	4d	Thu 3/27/97	Tue 4/1/97
136	Build Server Resources	3d	Thu 3/27/97	Mon 3/31/97
137	Build FS2 User Accounts/User Groups	3d	Thu 3/27/97	Mon 3/31/97
138	Build FS2 Printer Queues	3d	Thu 3/27/97	Mon 3/31/97
139	Build Required Exchange Public Folders	3d	Thu 3/27/97	Mon 3/31/97
140	Build Required NT Shares	3d	Thu 3/27/97	Mon 3/31/97
141	Migrate cc:Mail	1d	Tue 4/1/97	Tue 4/1/97
142	Update Exchange Accounts w/ cc:Mail Inf.	1d	Tue 4/1/97	Tue 4/1/97
143	Migrate cc:Mail server Inf.	1d	Tue 4/1/97	Tue 4/1/97
144	Forward cc:Mail to Exchange Accounts	1d	Tue 4/1/97	Tue 4/1/97
145	Migrate SECNAV Server Data	1d	Tue 4/1/97	Tue 4/1/97
146	Migrate FS2 Group Data Shares	1d	Tue 4/1/97	Tue 4/1/97
147	Migrate FS2 Data Shares	1d	Tue 4/1/97	Tue 4/1/97
148	Modify FS2 User Workstations	2d	Tue 4/1/97	Wed 4/2/97
149	Configure Workstations	1d	Tue 4/1/97	Tue 4/1/97
150	Remove SECNAV PC Image	1d	Tue 4/1/97	Tue 4/1/97
151	Install DNHN PC Image	1d	Tue 4/1/97	Tue 4/1/97
152	Install Exchange SP2	1d	Tue 4/1/97	Tue 4/1/97
153	Q/A FS2 PCs	1d	Wed 4/2/97	Wed 4/2/97
154	Log Into DNHN	1d	Wed 4/2/97	Wed 4/2/97
155	Log into Exchange	1d	Wed 4/2/97	Wed 4/2/97

Project: SECNAV Migration without Date: Thu 3/27/97	Task		Rolled Up Task	
	Progress		Rolled Up Milestone	
	Milestone		Rolled Up Progress	
	Summary			

Page 5

ID	Task Name	Duration	Start	Finish
156	Map and Print to FS2 DNHN Printers	1d	Wed 4/2/97	Wed 4/2/97
157	Test Applications	1d	Wed 4/2/97	Wed 4/2/97
158	Sign off On PCs	1d	Wed 4/2/97	Wed 4/2/97
159	Migrate FS18, ASN I&E	7d	Wed 3/12/97	Thu 3/20/97
160	Build Server Resources	6d	Wed 3/12/97	Wed 3/19/97
161	Build I&E User Accounts/User Groups	6d	Wed 3/12/97	Wed 3/19/97
162	Build I&E Printer Queues	6d	Wed 3/12/97	Wed 3/19/97
163	Build Required Exchange Public Folders	6d	Wed 3/12/97	Wed 3/19/97
164	Build Required NT Shares	6d	Wed 3/12/97	Wed 3/19/97
165	Migrate cc:Mail	1d	Thu 3/20/97	Thu 3/20/97
166	Update Exchange Accounts w/ cc:Mail Inf.	1d	Thu 3/20/97	Thu 3/20/97
167	Migrate cc:Mail server Inf.	1d	Thu 3/20/97	Thu 3/20/97
168	Forward cc:Mail to Exchange Accounts	1d	Thu 3/20/97	Thu 3/20/97
169	Migrate SECNAV Server Data	1d	Thu 3/20/97	Thu 3/20/97
170	Migrate I&E Group Data Shares	1d	Thu 3/20/97	Thu 3/20/97
171	Migrate I&E Data Shares	1d	Thu 3/20/97	Thu 3/20/97
172	Modify I&E User Workstations	2d	Thu 3/20/97	Fri 3/21/97
173	Configure Workstations	1d	Thu 3/20/97	Thu 3/20/97
174	Remove SECNAV PC Image	1d	Thu 3/20/97	Thu 3/20/97
175	Install DNHN PC Image	1d	Thu 3/20/97	Thu 3/20/97
176	Install Exchange SP2	1d	Thu 3/20/97	Thu 3/20/97
177	Q/A I&E PCs	1d	Fri 3/21/97	Fri 3/21/97
178	Log Into DNHN	1d	Fri 3/21/97	Fri 3/21/97
179	Log into Exchange	1d	Fri 3/21/97	Fri 3/21/97
180	Map and Print to I&E DNHN Printers	1d	Fri 3/21/97	Fri 3/21/97
181	Test Applications	1d	Fri 3/21/97	Fri 3/21/97
182	Sign off On PCs	1d	Fri 3/21/97	Fri 3/21/97
183	Migrate FS7,	4d	Mon 3/31/97	Thu 4/3/97
184	Build Server Resources	3d	Mon 3/31/97	Wed 4/2/97
185	Build FS7 User Accounts/User Groups	3d	Mon 3/31/97	Wed 4/2/97
186	Build FS7 Printer Queues	3d	Mon 3/31/97	Wed 4/2/97

Project: SECNAV Migration without
Date: Thu 3/27/97

Task

Progress

Milestone

Summary

Rolled Up Task

Rolled Up Milestone

Rolled Up Progress

ID	Task Name	Duration	Start	Finish
187	Build Required Exchange Public Folders	3d	Mon 3/31/97	Wed 4/2/97
188	Build Required NT Shares	3d	Mon 3/31/97	Wed 4/2/97
189	Migrate cc:Mail	1d	Thu 4/3/97	Thu 4/3/97
190	Update Exchange Accounts w/ cc:Mail Inf.	1d	Thu 4/3/97	Thu 4/3/97
191	Migrate cc:Mail server Inf.	1d	Thu 4/3/97	Thu 4/3/97
192	Forward cc:Mail to Exchange Accounts	1d	Thu 4/3/97	Thu 4/3/97
193	Migrate SECNAV Server Data	1d	Thu 4/3/97	Thu 4/3/97
194	Migrate FS7 Group Data Shares	1d	Thu 4/3/97	Thu 4/3/97
195	Migrate FS7 Data Shares	1d	Thu 4/3/97	Thu 4/3/97
196	Modify FS7 User Workstations	2d	Thu 4/3/97	Fri 4/4/97
197	Configure Workstations	1d	Thu 4/3/97	Thu 4/3/97
198	Remove SECNAV PC Image	1d	Thu 4/3/97	Thu 4/3/97
199	Install DNHN PC Image	1d	Thu 4/3/97	Thu 4/3/97
200	Install Exchange SP2	1d	Thu 4/3/97	Thu 4/3/97
201	Q/A FS7 PCs	1d	Fri 4/4/97	Fri 4/4/97
202	Log Into DNHN	1d	Fri 4/4/97	Fri 4/4/97
203	Log into Exchange	1d	Fri 4/4/97	Fri 4/4/97
204	Map and Print to FS7 DNHN Printers	1d	Fri 4/4/97	Fri 4/4/97
205	Test Applications	1d	Fri 4/4/97	Fri 4/4/97
206	Sign off On PCs	1d	Fri 4/4/97	Fri 4/4/97
207	Migrate FS12,	4d	Thu 4/3/97	Tue 4/8/97
208	Build Server Resources	3d	Thu 4/3/97	Mon 4/7/97
209	Build FS12 User Accounts/User Groups	3d	Thu 4/3/97	Mon 4/7/97
210	Build FS12 Printer Queues	3d	Thu 4/3/97	Mon 4/7/97
211	Build Required Exchange Public Folders	3d	Thu 4/3/97	Mon 4/7/97
212	Build Required NT Shares	3d	Thu 4/3/97	Mon 4/7/97
213	Migrate cc:Mail	1d	Tue 4/8/97	Tue 4/8/97
214	Update Exchange Accounts w/ cc:Mail Inf.	1d	Tue 4/8/97	Tue 4/8/97
215	Migrate cc:Mail server Inf.	1d	Tue 4/8/97	Tue 4/8/97
216	Forward cc:Mail to Exchange Accounts	1d	Tue 4/8/97	Tue 4/8/97
217	Migrate SECNAV Server Data	1d	Tue 4/8/97	Tue 4/8/97

Project: SECNAV Migration without
Date: Thu 3/27/97

Task

Progress

Milestone

Summary

Rolled Up Task

Rolled Up Milestone

Rolled Up Progress

ID	Task Name	Duration	Start	Finish
218	Migrate FS12 Group Data Shares	1d	Tue 4/8/97	Tue 4/8/97
219	Migrate FS12 Data Shares	1d	Tue 4/8/97	Tue 4/8/97
220	Modify FS12 User Workstations	2d	Tue 4/8/97	Wed 4/9/97
221	Configure Workstations	1d	Tue 4/8/97	Tue 4/8/97
222	Remove SECNAV PC Image	1d	Tue 4/8/97	Tue 4/8/97
223	Install DNHN PC Image	1d	Tue 4/8/97	Tue 4/8/97
224	Install Exchange SP2	1d	Tue 4/8/97	Tue 4/8/97
225	Q/A FS12 PCs	1d	Wed 4/9/97	Wed 4/9/97
226	Log Into DNHN	1d	Wed 4/9/97	Wed 4/9/97
227	Log into Exchange	1d	Wed 4/9/97	Wed 4/9/97
228	Map and Print to FS12 DNHN Printers	1d	Wed 4/9/97	Wed 4/9/97
229	Test Applications	1d	Wed 4/9/97	Wed 4/9/97
230	Sign off On PCs	1d	Wed 4/9/97	Wed 4/9/97
231	Migrate FS10,	4d	Thu 4/10/97	Tue 4/15/97
232	Build Server Resources	3d	Thu 4/10/97	Mon 4/14/97
233	Build FS10 User Accounts/User Groups	3d	Thu 4/10/97	Mon 4/14/97
234	Build FS10 Printer Queues	3d	Thu 4/10/97	Mon 4/14/97
235	Build Required Exchange Public Folders	3d	Thu 4/10/97	Mon 4/14/97
236	Build Required NT Shares	3d	Thu 4/10/97	Mon 4/14/97
237	Migrate cc:Mail	1d	Tue 4/15/97	Tue 4/15/97
238	Update Exchange Accounts w/ cc:Mail Inf.	1d	Tue 4/15/97	Tue 4/15/97
239	Migrate cc:Mail server Inf.	1d	Tue 4/15/97	Tue 4/15/97
240	Forward cc:Mail to Exchange Accounts	1d	Tue 4/15/97	Tue 4/15/97
241	Migrate SECNAV Server Data	1d	Tue 4/15/97	Tue 4/15/97
242	Migrate FS10 Group Data Shares	1d	Tue 4/15/97	Tue 4/15/97
243	Migrate FS10 Data Shares	1d	Tue 4/15/97	Tue 4/15/97
244	Modify FS10 User Workstations	2d	Tue 4/15/97	Wed 4/16/97
245	Configure Workstations	1d	Tue 4/15/97	Tue 4/15/97
246	Remove SECNAV PC Image	1d	Tue 4/15/97	Tue 4/15/97
247	Install DNHN PC Image	1d	Tue 4/15/97	Tue 4/15/97
248	Install Exchange SP2	1d	Tue 4/15/97	Tue 4/15/97

Project: SECNAV Migration without
Date: Thu 3/27/97

Task

Progress

Milestone

Summary

Rolled Up Task

Rolled Up Milestone

Rolled Up Progress

ID	Task Name	Duration	Start	Finish
249	Q/A FS10 PCs	1d	Wed 4/16/97	Wed 4/16/97
250	Log Into DNHN	1d	Wed 4/16/97	Wed 4/16/97
251	Log into Exchange	1d	Wed 4/16/97	Wed 4/16/97
252	Map and Print to FS10 DNHN Printers	1d	Wed 4/16/97	Wed 4/16/97
253	Test Applications	1d	Wed 4/16/97	Wed 4/16/97
254	Sign off On PCs	1d	Wed 4/16/97	Wed 4/16/97

Project: SECNAV Migration without
Date: Thu 3/27/97

Task

Progress

Milestone

Summary


◆

Rolled Up Task

Rolled Up Milestone

Rolled Up Progress

◇

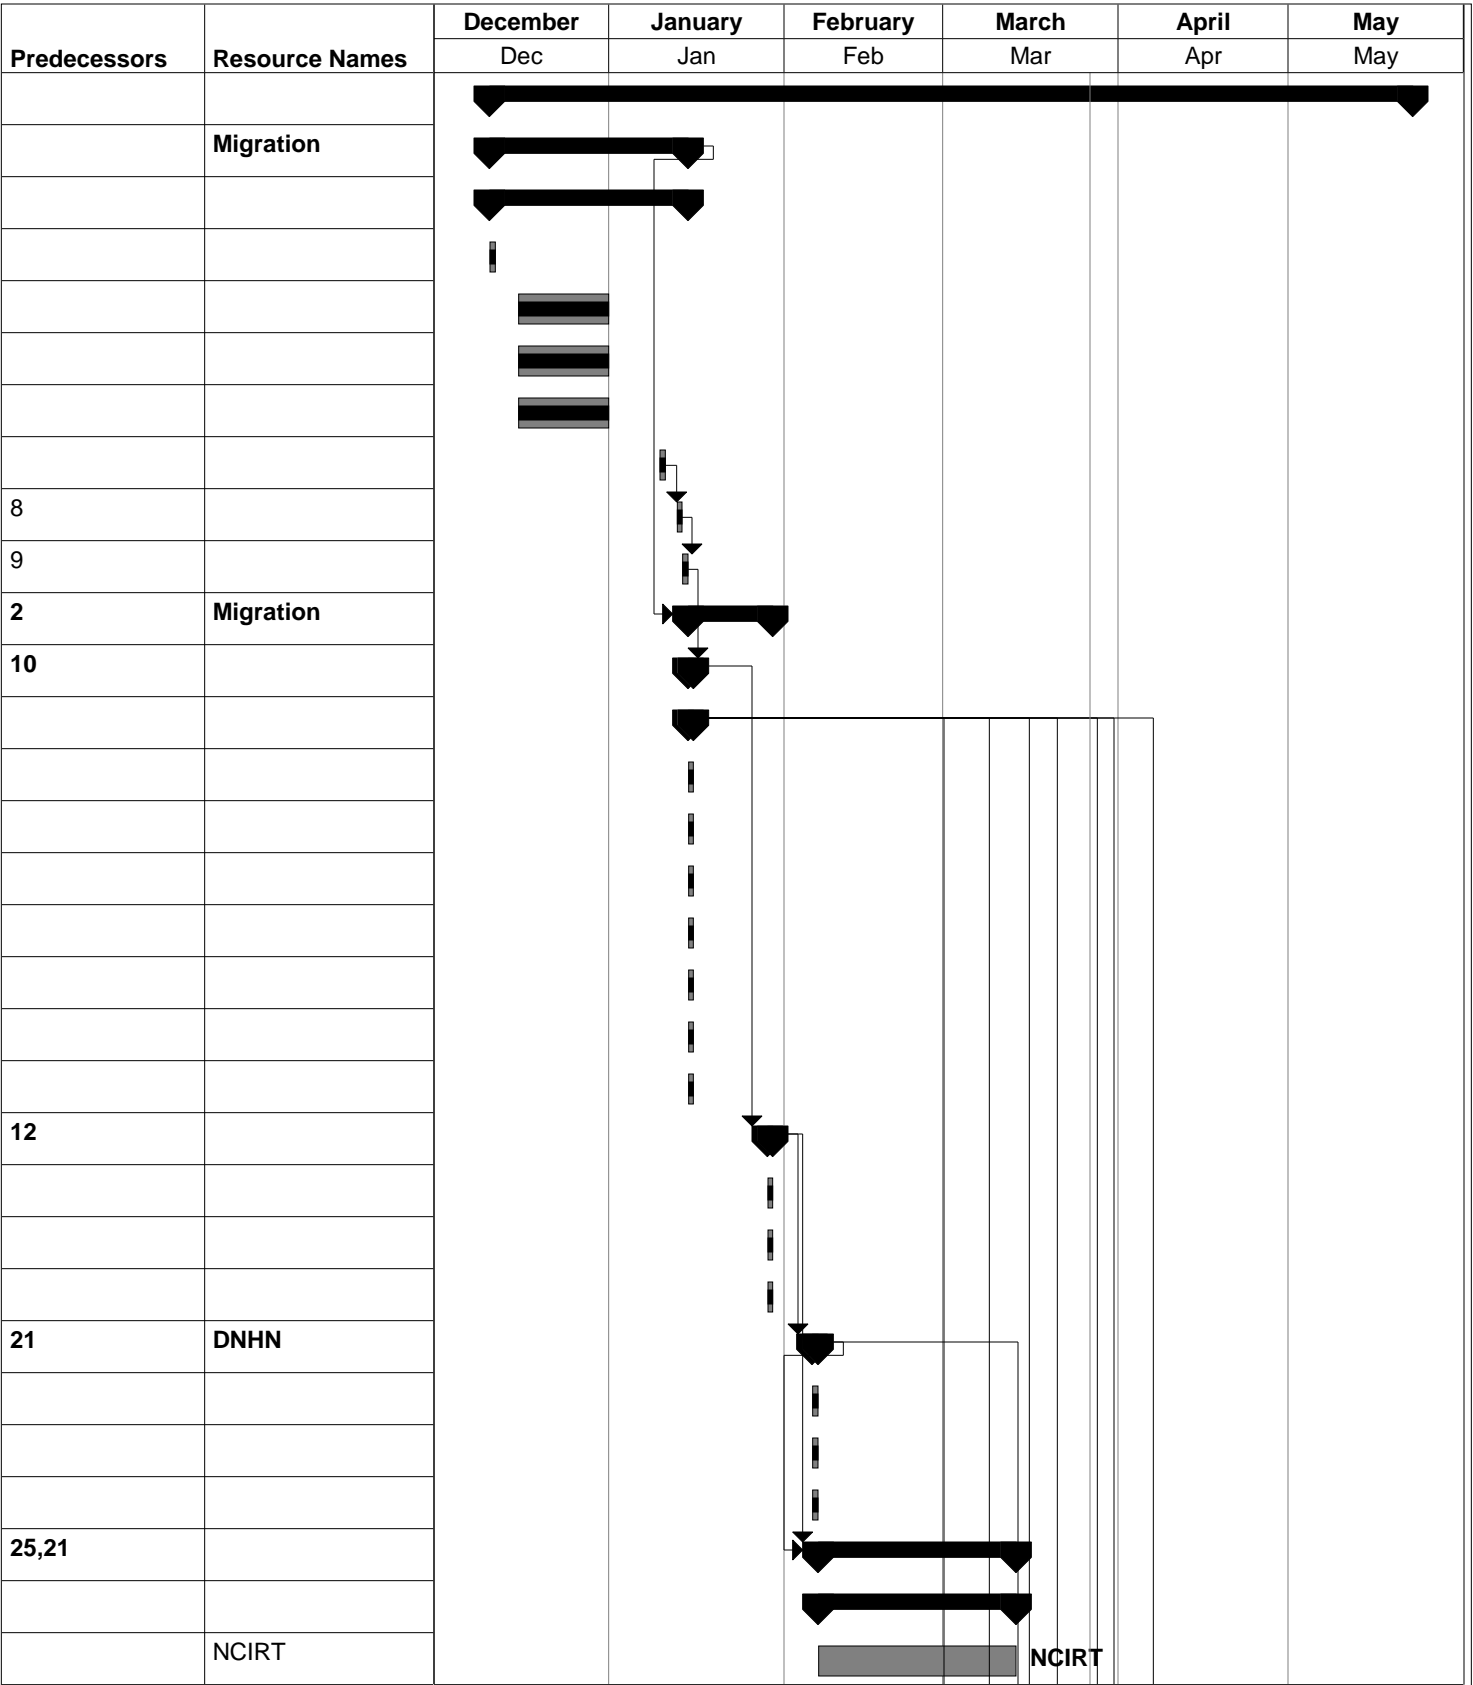

Project: SECNAV Migration without
Date: Thu 3/27/97

Task

Progress

Milestone


Summary

Rolled Up Task

Rolled Up Milestone

Rolled Up Progress

Page 10

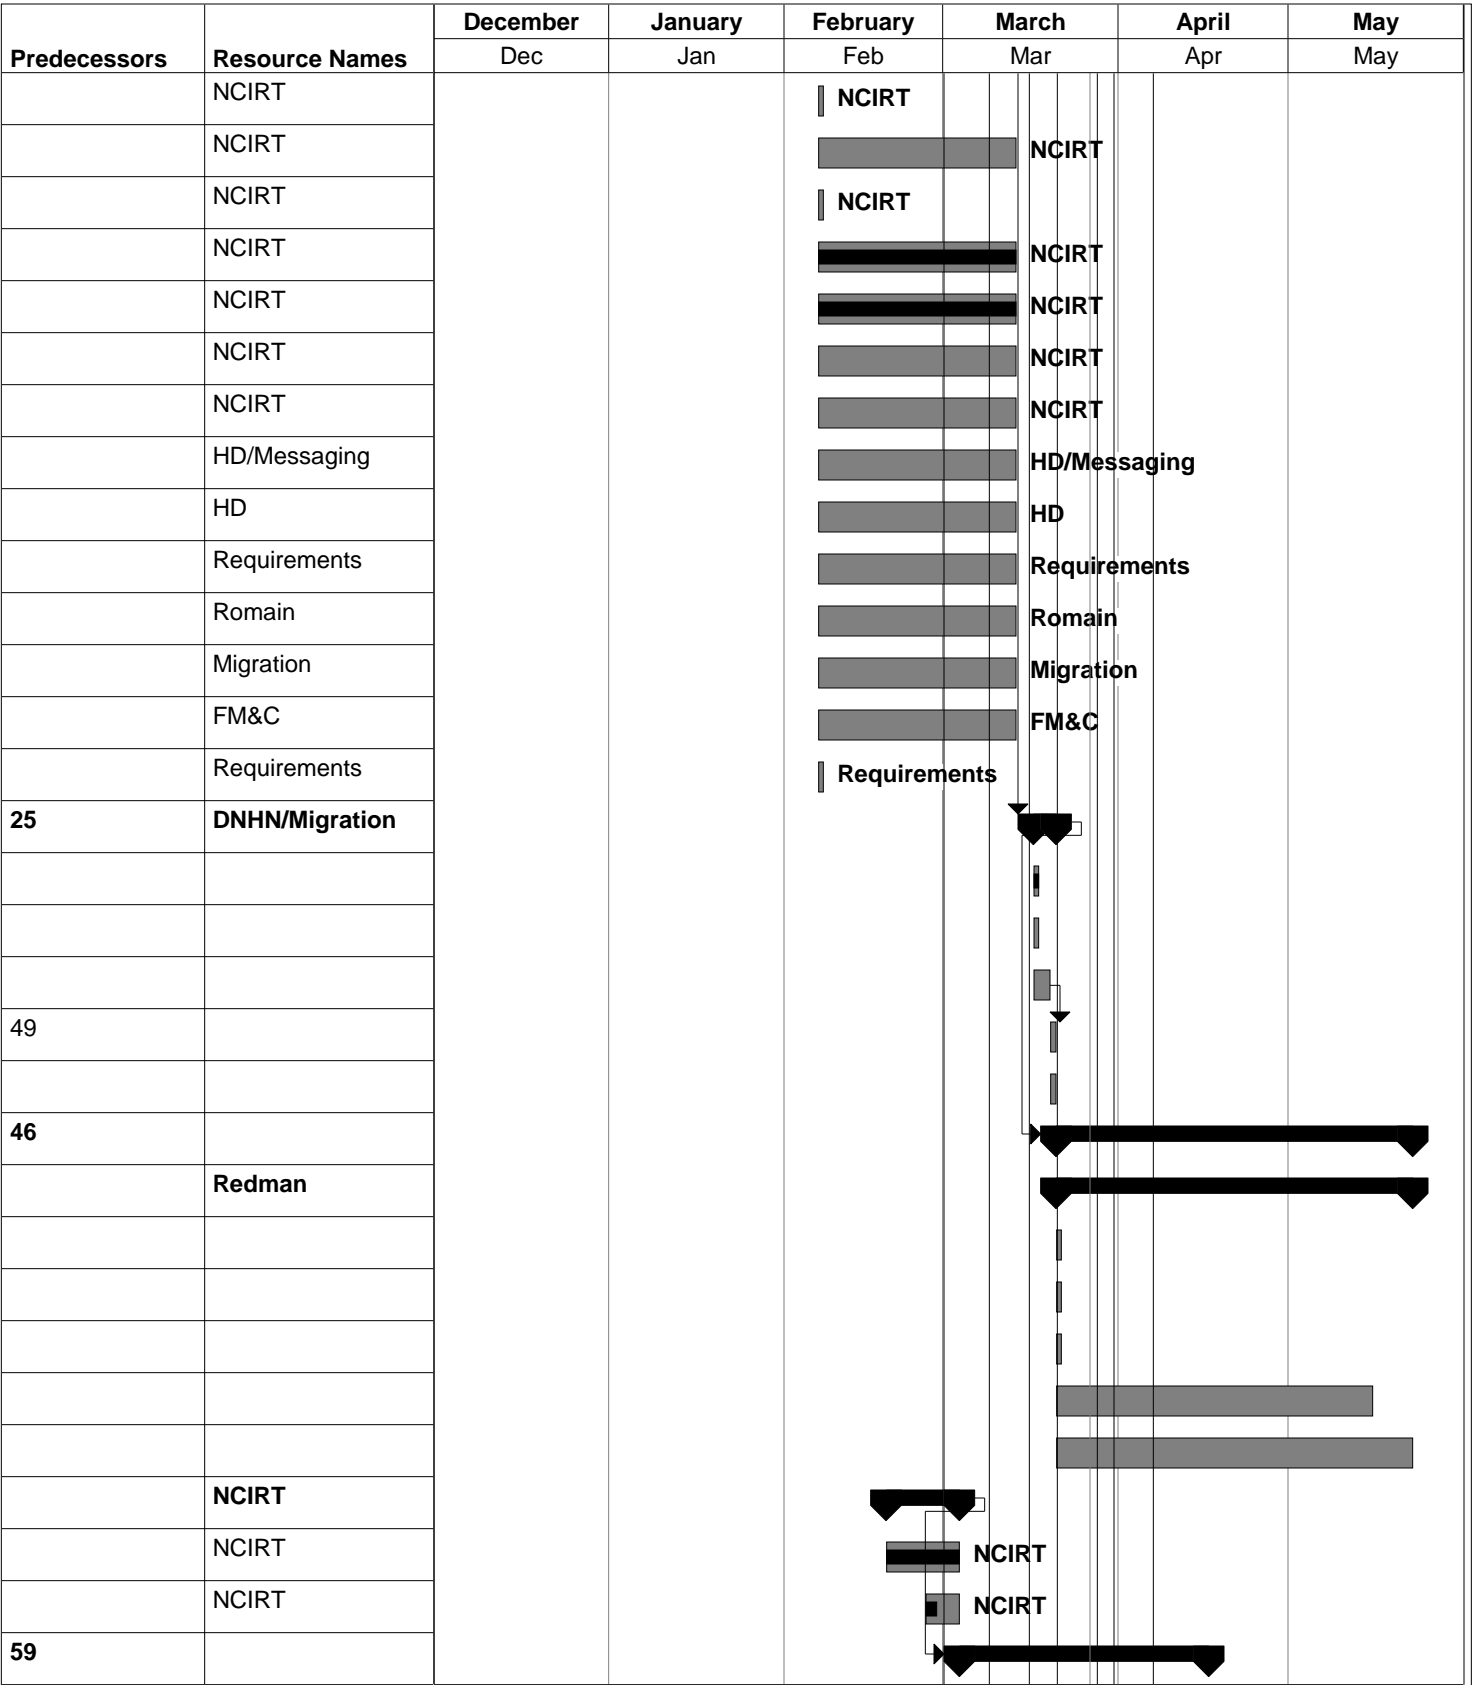

Project: SECNAV Migration without
Date: Thu 3/27/97

Task

Progress

Milestone

Summary

◆

Rolled Up Task

Rolled Up Milestone

Rolled Up Progress

◇

Predecessors	Resource Names	December	January	February	March	April	May
		Dec	Jan	Feb	Mar	Apr	May
	HD/Messaging					HD/Messaging	
	HD/Messaging					HD/Messaging	
	HD/Messaging					HD/Messaging	
88	HD/Server						
	HD/Server					HD/Server	
	HD/Server					HD/Server	
88	Migration						
	Migration					Migration	
	Migration					Migration	
	Migration					Migration	
88,101	Migration/QA						
	Migration/QA					Migration/QA	
	Migration/QA					Migration/QA	
	Migration/QA					Migration/QA	
	Migration/QA					Migration/QA	
	Migration/QA					Migration/QA	
13							
	HD/Server					HD/Server	
	HD/Server					HD/Server	
	HD/Messaging					HD/Messaging	
	HD/Server					HD/Server	
112	HD/Messaging						
	HD/Messaging					HD/Messaging	
	HD/Messaging					HD/Messaging	
	HD/Messaging					HD/Messaging	
112	HD/Server						
	HD/Server					HD/Server	
	HD/Server					HD/Server	

Project: SECNAV Migration without Date: Thu 3/27/97

Task

Progress

Milestone

Summary

Rolled Up Task

Rolled Up Milestone

Rolled Up Progress

Predecessors	Resource Names	December	January	February	March	April	May
		Dec	Jan	Feb	Mar	Apr	May
112	Migration						
	Migration						
	Migration						
	Migration						
112,125	Migration/QA						
	Migration/QA						
	Migration/QA						
	Migration/QA						
	Migration/QA						
	Migration/QA						
112							
	HD/Server						
	HD/Server						
	HD/Messaging						
	HD/Server						
136	HD/Messaging						
	HD/Messaging						
	HD/Messaging						
	HD/Messaging						
136	HD/Server						
	HD/Server						
	HD/Server						
136	Migration						
	Migration						
	Migration						
	Migration						
149	Migration/QA						
	Migration/QA						
	Migration/QA						

Project: SECNAV Migration without Date: Thu 3/27/97

Task

Progress

Milestone
































Summary








Rolled Up Task

Rolled Up Milestone

Rolled Up Progress

Page 14

Predecessors	Resource Names	December	January	February	March	April	May
		Dec	Jan	Feb	Mar	Apr	May
	HD/Messaging						HD/Messaging
	HD/Server						HD/Server
184	HD/Messaging						
	HD/Messaging						HD/Messaging
	HD/Messaging						HD/Messaging
	HD/Messaging						HD/Messaging
184	HD/Server						
	HD/Server						HD/Server
	HD/Server						HD/Server
							
184	Migration						
	Migration						Migration
	Migration						Migration
	Migration						Migration
197	Migration/QA						
	Migration/QA						Migration/QA
	Migration/QA						Migration/QA
	Migration/QA						Migration/QA
	Migration/QA						Migration/QA
	Migration/QA						Migration/QA
							
13							
	HD/Server						HD/Server
	HD/Server						HD/Server
	HD/Messaging						HD/Messaging
	HD/Server						HD/Server
208	HD/Messaging						
	HD/Messaging						HD/Messaging
	HD/Messaging						HD/Messaging
	HD/Messaging						HD/Messaging
208	HD/Server						

Project: SECNAV Migration without Date: Thu 3/27/97	Task		Rolled Up Task	
	Progress		Rolled Up Milestone	
	Milestone		Rolled Up Progress	
	Summary			
Page 16				

Predecessors	Resource Names	December	January	February	March	April	May
		Dec	Jan	Feb	Mar	Apr	May
	HD/Server					HD/Server	
	HD/Server					HD/Server	
208	Migration						
	Migration					Migration	
	Migration					Migration	
	Migration					Migration	
221	Migration/QA						
	Migration/QA					Migration/QA	
	Migration/QA					Migration/QA	
	Migration/QA					Migration/QA	
	Migration/QA					Migration/QA	
	Migration/QA					Migration/QA	
13							
	HD/Server					HD/Server	
	HD/Server					HD/Server	
	HD/Messaging					HD/Messaging	
	HD/Server					HD/Server	
233	HD/Messaging						
	HD/Messaging					HD/Messaging	
	HD/Messaging					HD/Messaging	
	HD/Messaging					HD/Messaging	
233	HD/Server						
	HD/Server					HD/Server	
	HD/Server					HD/Server	
233	Migration						
	Migration					Migration	
	Migration					Migration	
	Migration					Migration	

Project: SECNAV Migration without Date: Thu 3/27/97

Task

Progress







Milestone

Summary

Rolled Up Task





Rolled Up Milestone



Rolled Up Progress

Predecessors	Resource Names	December	January	February	March	April	May
		Dec	Jan	Feb	Mar	Apr	May
245	Migration/QA						
	Migration/QA					 Migration/QA	
	Migration/QA					 Migration/QA	
	Migration/QA					 Migration/QA	
	Migration/QA					 Migration/QA	
	Migration/QA					 Migration/QA	



Project: SECNAV Migration without
 Date: Thu 3/27/97

Task 
 Progress 
 Milestone 
 Summary 

Rolled Up Task 
 Rolled Up Milestone 
 Rolled Up Progress 
